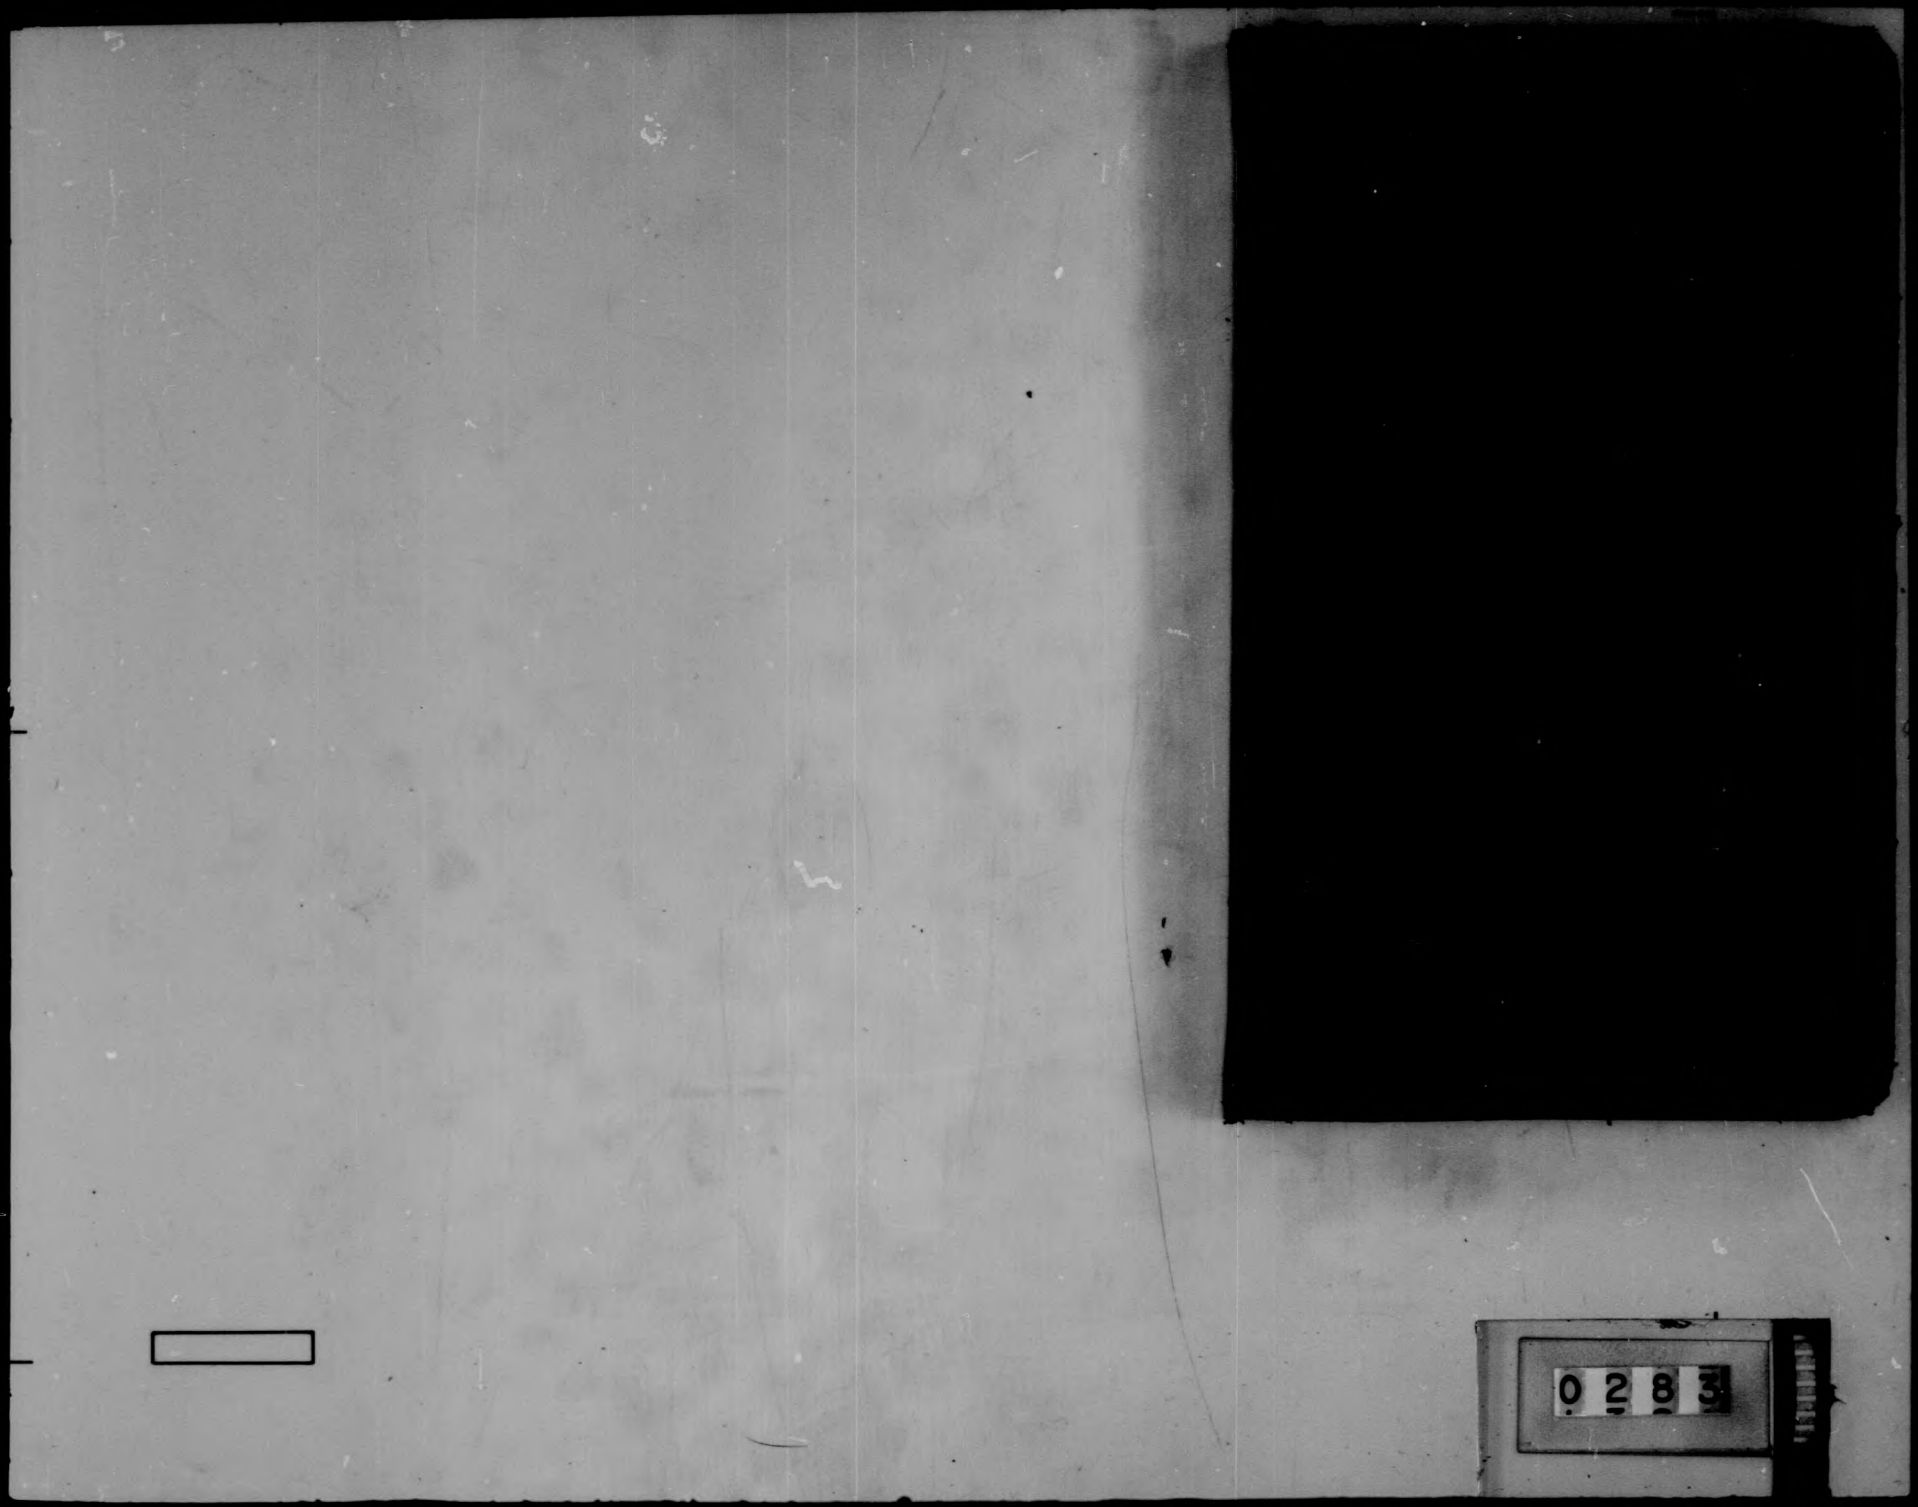
0283

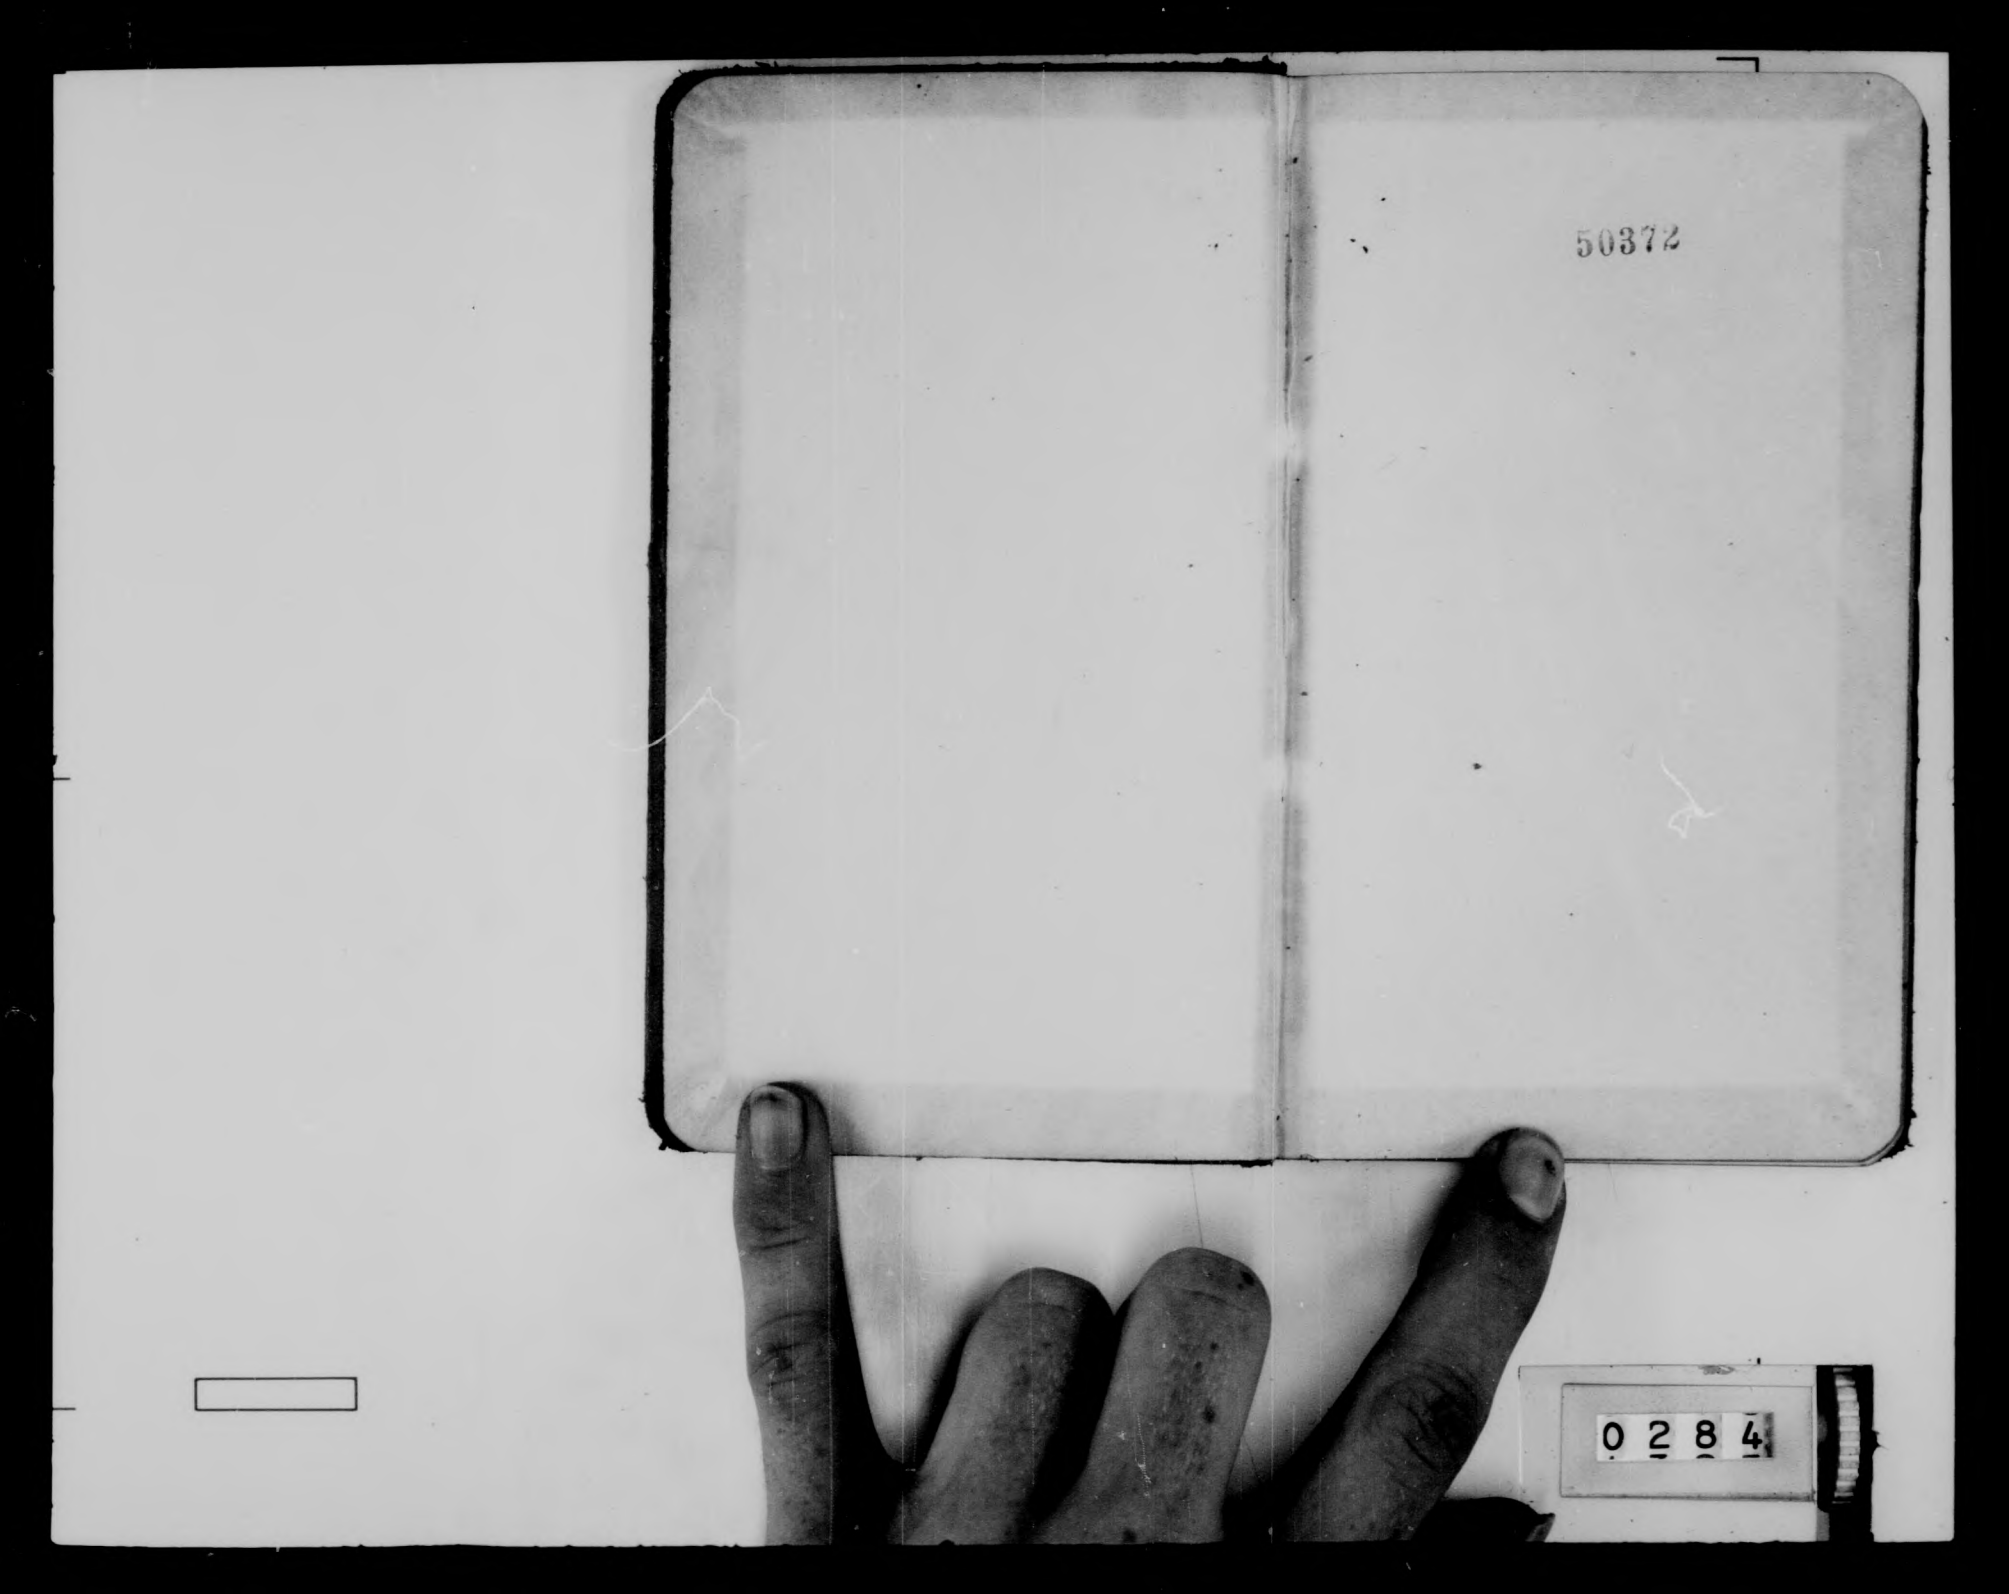
50372
0284

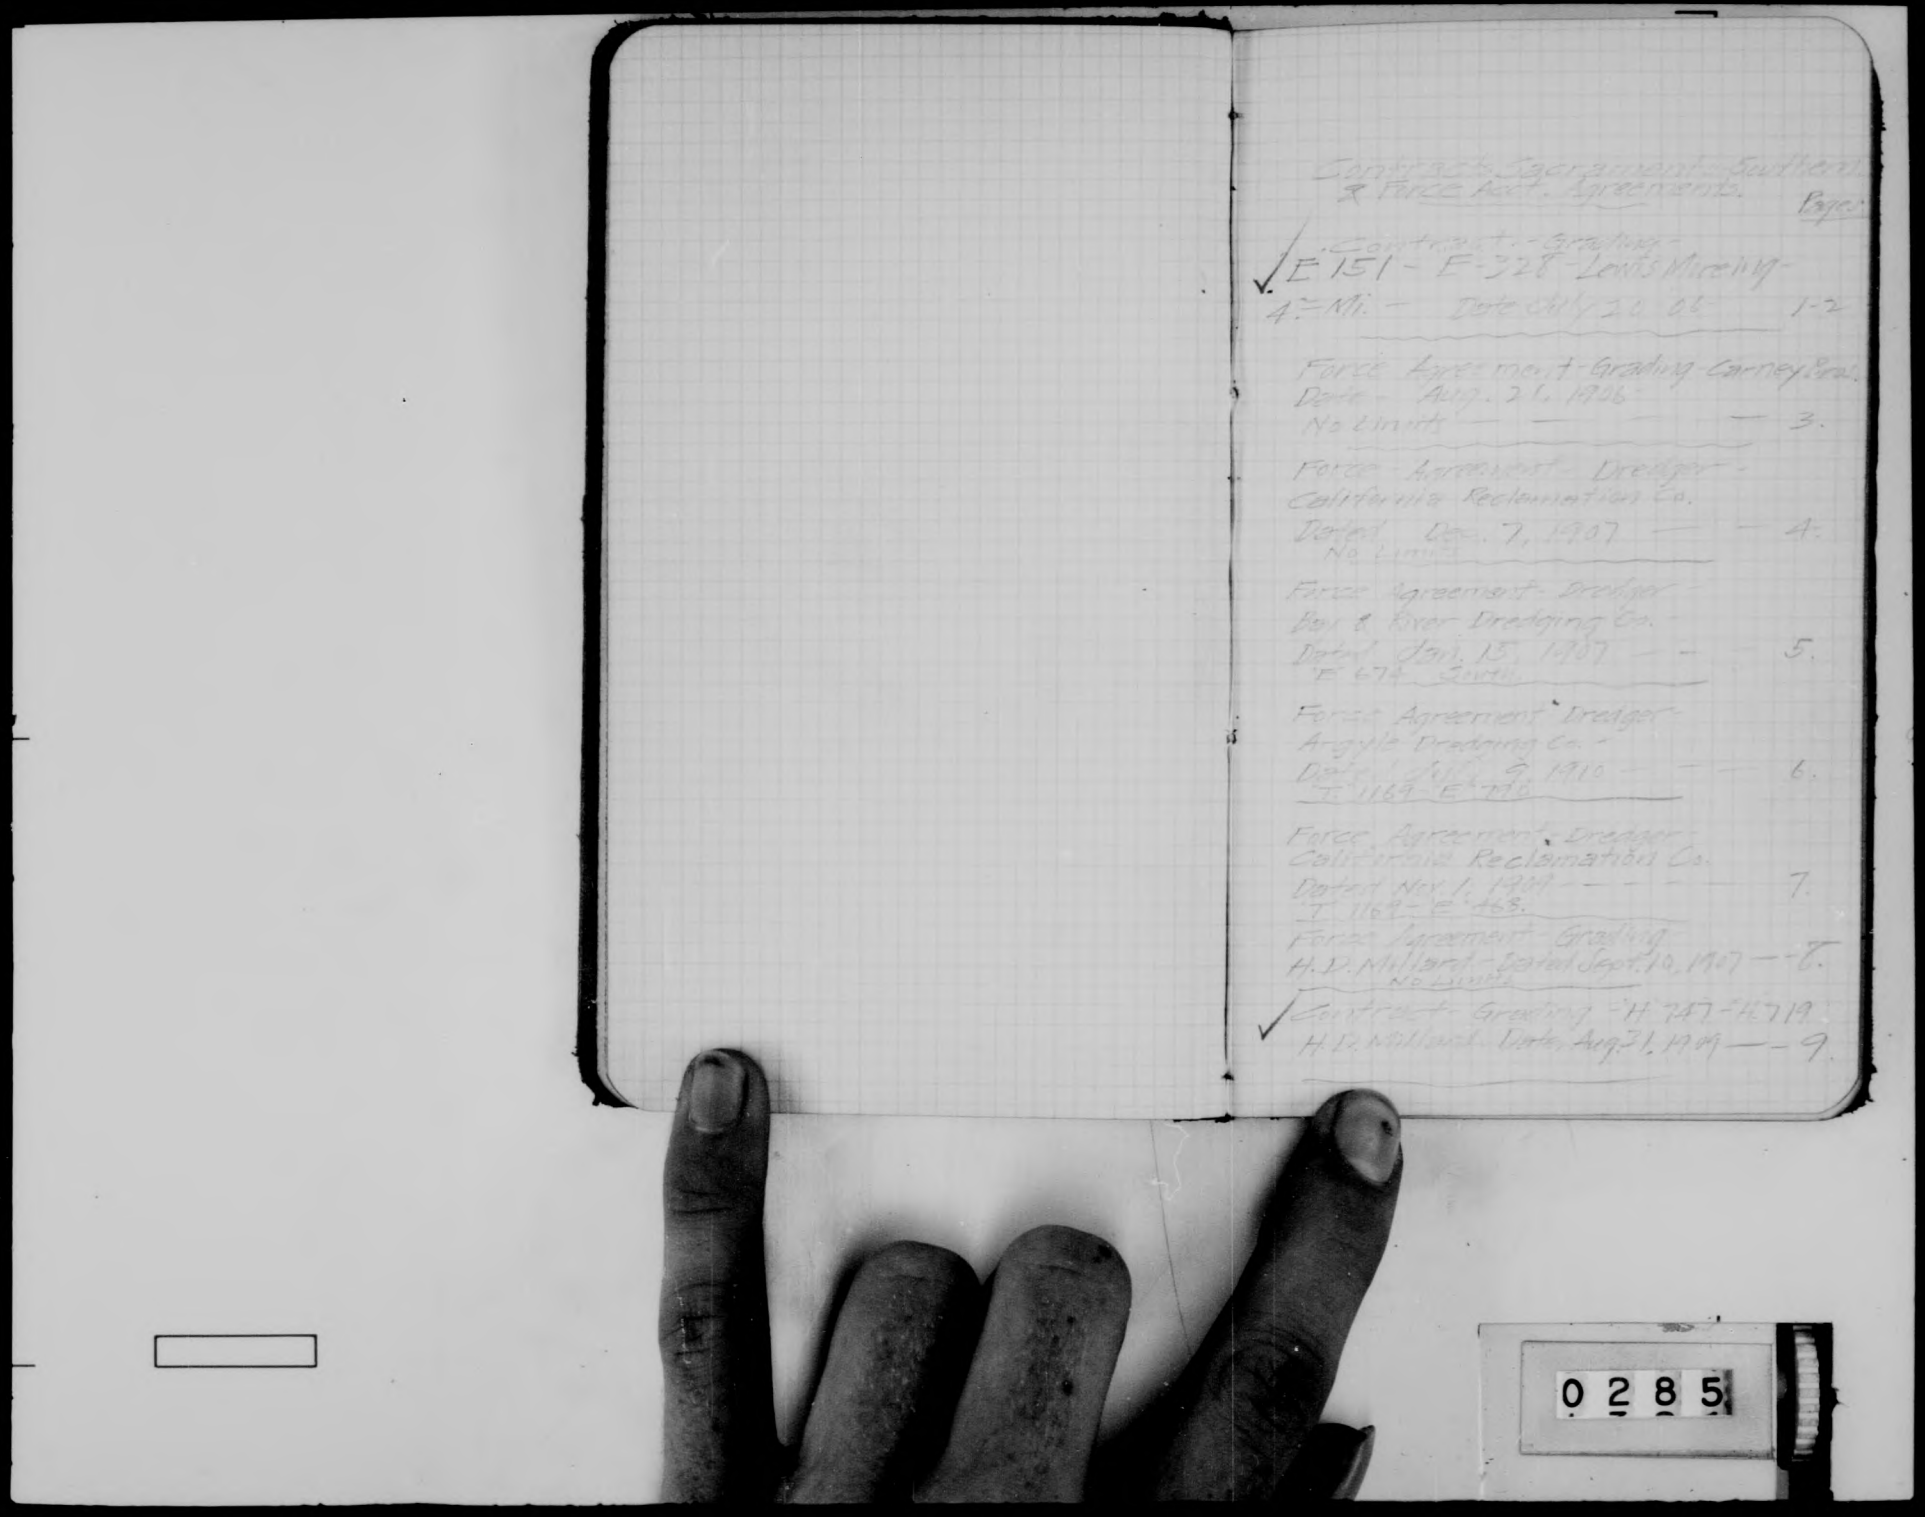
Contracts Sacramento - Southern
R Force Acct. Agreements.
Page
Contract - Grading -
E 151 - E 328 - Lents Mccoy -
4 = Mi. - Date July 20 06 1-2
Force Agreement - Grading - Carney Bros.
Date - Aug. 21, 1906
No Limits — — — — 3.
Force Agreement - Dredger -
California Reclamation Co.
Dated Dec. 7, 1907 — — 4.
No Limits
Force Agreement - Dredger -
Bay & River Dredging Co.
Dated Jan. 13, 1907 — — 5.
F 674 - South
Force Agreement - Dredger -
Argyle Dredging Co.
Dated July 9, 1910 — — 6.
I 1169 - E 146
Force Agreement - Dredger -
California Reclamation Co.
Dated Nov 1, 1911 — — — 7.
I 1169 - E 463.
Force Agreement - Grading -
H. D. Millard - Dated Sept. 10, 1907 — — 8.
No Limits
Contract - Grading - H 757 - H 719
H. D. Millard. Date, Aug 21, 1909 — — 9.
0285

(1)

Sacramento Southern.

Contract - P.400. Book "Estimates"

Grading - Sacramento Southern 4.2 Miles - Sta. "E" 151+10 to "E" 328+00. - Sacramento County, - Calif.

Lewis Moreing - Contractor

Date: July 20, 1906.

For material of any kind encountered in excavation and in borrow-pits used for obtaining material to form embankments. -

Thirty-three cents per cubic yard - 23¢ per cu. yd.

For hauling excavated material a distance in excess of four hundred (400) feet, one cent (0.01) per cubic yard

(1)

per one hundred (100) feet excess of haul.

Gross haul shall be measured between the centers of masses of the material as excavated and of the same material as deposited in the embankments.

Net or paid haul is four hundred (400) feet less than gross haul.

Cuts and borrow pits and excavations for foundations of masonry and timber bridges and trestles, box culverts and all other structures if not under water to require bailing or pumping; and all surface ditches, wagon road diversions and wagon and farm road crossings, and all other grading shall be made as

0286

(2)

directed by the Engineer, and shall be paid for at the prices hereinbefore specified.

Quantities paid for shall be measured in excavation of cuts and borrow pits.

0287

Force Account Agreement: Grading
Carney Brothers - "P300 - Book 4 Estimate"
Dated Aug. 21, 1906.

"to grade - - such portions of the main line and sidings appertaining - - to Sacramento Southern Railroad, extending from Sacramento toward Walnut Grove, State of California."

"Cost of Labor and teams with appliances for grading and appertaining thereto and ten (10) per cent in addition to cover use and repair of appliances and tools and cost of superintendence.
Cost of mess camp - without proprietary
No charge for camp & corral fence or damages to livestock

Explosives - cost on board cars plus 4¢ lb. for powder no addition to cost of caps and fuse.
S.P.Co. to pay transportation of own lines, men, outfit, explosives and tools in State of California, also hay, grain & coal from points in CAL. - West of San Fran.
No charge for land or water for use.

0288

4.

Dredger. Force Acct. Agreement.
California Reclamation Co.
"P 360 - Book 3 - Estimates."
Dated Dec. 3, 1907

Dredger "San Francisco."
@ $175.00 per day.
dt. Dec. 5, to Dec. 15, 1907.

4.

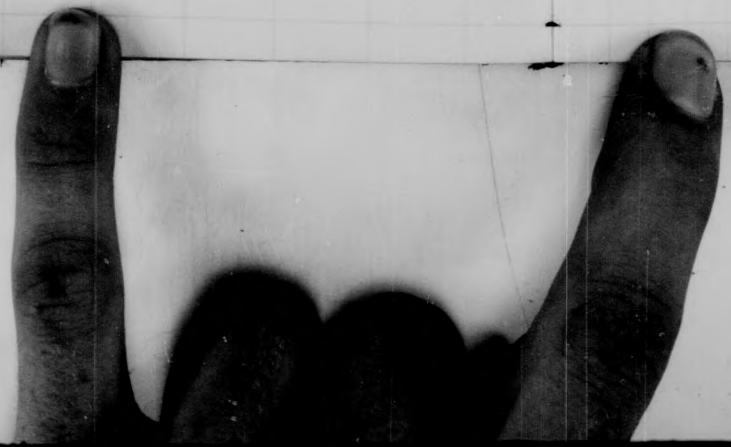

5.

Dredger - Force Acct. Agreement -
Bay & River Dredging Co.
"P.400 - Book 3 - Estimates"
Dated Jan 15. 1907
Dredging on E of Hay
southerly from Sta. E 674.
Sac. Southern Railroad
Steam Shovel Dredge "MOGUL"
Equipped as steamshovel - 75. per
22 hr. day.
Equipped with boom & bucket 80.00
per 22 hr. day.

5.

0290

(6.)

Dredger Force Account Agreement.
Argyle Dredging Co.
"P. 450 - Book 16"
Dated July 9, 1910.
Dredging in Right of Way of
Sacramento Southern Railroad.
"from opposite Sta. "T" 1169
northerly to opposite Sta.
"E" 790+, and being from
the North arm of the levee
of Reclamation District No. 554
to opposite Sta. "E" 790+.
Clamshell dredger "Argyle."

$140.00 per day of 22 hrs.

(6.)

0291

Dredger - Force Account Agreement.
California Reclamation Co.
"P. 125 - Book 13 -"
Dated Nov. 1. 1909.
Dredging on R. of Way of
Sac. Southern Railroad.
"from opposite Sta. "T" 1169
northerly to opp. Sta. "E" 468.
and being from the North arm
of the levee of Reclamation
District No. 554 to the
end of the dredger cut,
opposite Sta. E 468."
Sacramento County, CALIF.

135 ft. Suction Dredger - $125.00 per day 22 hrs.
155 " " " - $155.00 " " "
150 " " " - $150.00 " " "
if compelled to remain
idle for longer than 1 work-
day - $50 per day per dredger.

$150 per Mo. - Captain
"50 per " - 1 Deck Hand

0292

(8)

Force Account Agreement Grading.
H.D. Millard. "P.2 - Book 8."
Dated - Sept. 10, 1907.

Grading.

"Such portions as may be required - of Sacramento Southern Main Line and sidings

"cost of Labor and teams with appliances for grading and appertaining thereto and ten (10) per cent in addition to cover use and repair of appliances and tools and cost of superintendence."

remainder same as page 3.

(9)

0293

9.

Contract "P.28 - Book 19.

Grading Sacramento Southern -
0.5± Mile. - Sta. "H" 747+81.2 west
to "H" - 719+51.

Sacramento County - CALIF.
H. D. Millard, contractor.
Date, Aug. 31, 1909.

"Material of Any Kind encountered
in excav. and in bor. pits
used for obtain. mat. to form
embankments
21½¢ per cu. yd.
"for (O.H. etc.

Gross haul - etc.
Net " etc.
Cuts & bor. pits etc.

Overhaul for mixed material Bor.

9

0294
